ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors
1		**CASCADE WATERMAIN**	**255 days**	**Mon 10/10/22**	**Fri 9/29/23**		
2		TREE REMOVAL	0 days	Mon 10/10/22	Mon 10/10/22		
3		TRAFFIC CONTROL	1 day	Mon 10/10/22	Mon 10/10/22		4FF
4		SESC MESURES	1 day	Mon 10/10/22	Mon 10/10/22	3FF	5SS
5		STRIP TOPSOIL	2 days	Mon 10/10/22	Tue 10/11/22	4SS	7SS+1 day
6		**BURGER DR.**	**15 days**	**Tue 10/11/22**	**Mon 10/31/22**		
7		INSTALL W/M 9+10 - 23+55	6 days	Tue 10/11/22	Tue 10/18/22	5SS+1 day	14,8
8		REMOVE C/G @ TANGELWOOD	1 day	Wed 10/19/22	Wed 10/19/22	7	9
9		BUILD ROAD @ CROSSING	1 day	Thu 10/20/22	Thu 10/20/22	8	10
10		POUR C/G	1 day	Fri 10/21/22	Fri 10/21/22	9	11
11		GRADE DRIVES	2 days	Mon 10/24/22	Tue 10/25/22	10	12
12		PAVE DRIVES AND TANGLEWOOD CROSSING	1 day	Wed 10/26/22	Wed 10/26/22	11	13
13		POUR CONCRETE DRIVES	1 day	Thu 10/27/22	Thu 10/27/22	12	20
14		INSTALL W/M 26+10 - 36+21	4 days	Wed 10/19/22	Mon 10/24/22	7	15SS,18
15		RREMOVE C/G @ TUSCANY	1 day	Wed 10/19/22	Wed 10/19/22	14SS	16FF
16		BUILD ROAD @ CROSSING	1 day	Wed 10/19/22	Wed 10/19/22	15FF	17FF
17		POUR C/G	1 day	Wed 10/19/22	Wed 10/19/22	16FF	19
18		GRADE DRIVES	1 day	Tue 10/25/22	Tue 10/25/22	14	19
19		PAVE DRIVES AND TUSCANY CROSSING	1 day	Wed 10/26/22	Wed 10/26/22	18,17	20
20		WINTER CLEANUP	2 days	Fri 10/28/22	Mon 10/31/22	13,19	21
21		**WINTER SHUT DOWN**	**115 days**	**Mon 4/24/23**	**Fri 9/29/23**	**20**	
22		TRAFFIC CONTROL	1 day	Mon 4/24/23	Mon 4/24/23		23SS
23		SESC MESURES	1 day	Mon 4/24/23	Mon 4/24/23	22SS	24FF
24		STRIP TOPSOIL	1 day	Mon 4/24/23	Mon 4/24/23	23FF	25
25		START OF RIVER DRAW DOWN	4 days	Tue 4/25/23	Fri 4/28/23	24	26FF
26		SETUP FOR RIVER CROSSING	2 days	Thu 4/27/23	Fri 4/28/23	25FF	27SS+1 day
27		INSTALL W/M @ RIVER CROSSING	3 days	Fri 4/28/23	Mon 5/1/23	26SS+1 day	28
28		TNC W/M (BURGER DR.)	4 days	Tue 5/2/23	Fri 5/5/23	27	29
29		TIE IN W/M	1 day	Mon 5/8/23	Mon 5/8/23	28	30
30		INSTALL SERVICES	5 days	Tue 5/9/23	Mon 5/15/23	29	31
31		INSTALL STORM SEWER 30+45 - 11+75	6 days	Tue 5/16/23	Tue 5/23/23	30	33
32		**TUSCANY DR.**	**17 days**	**Wed 5/24/23**	**Thu 6/15/23**		

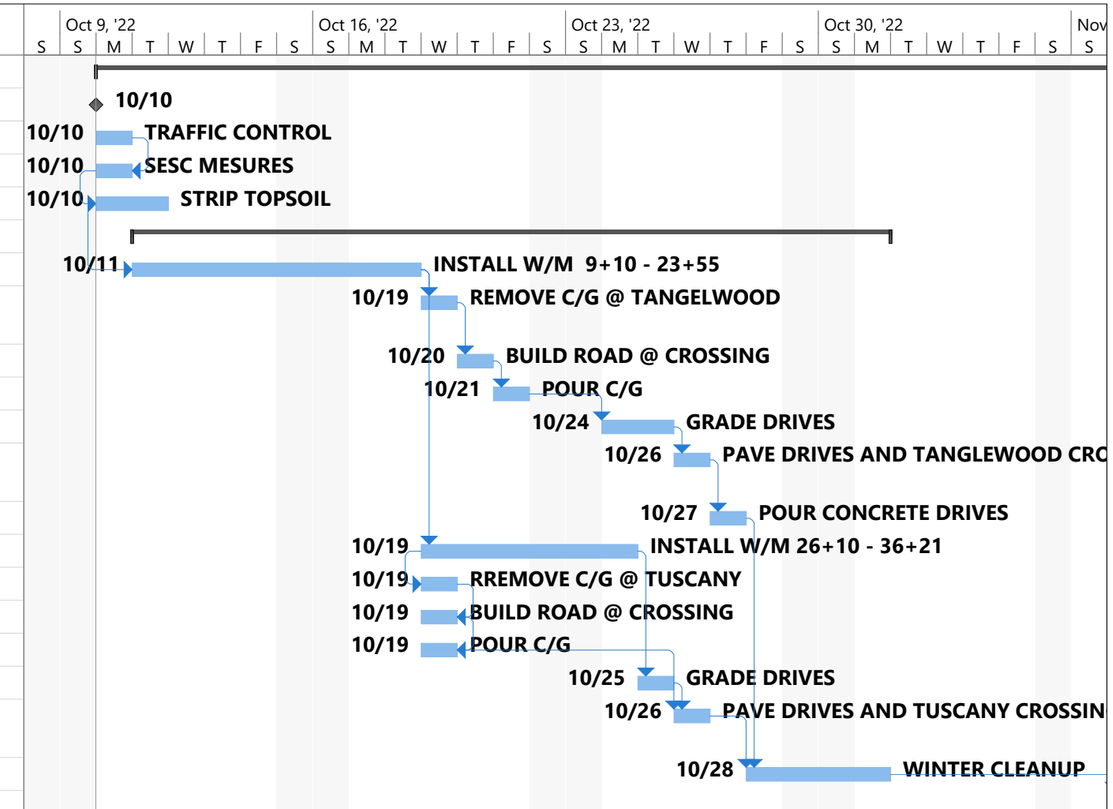

Project: Progress Schedule fall
Date: Tue 9/27/22

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors
33			INSTALL W/M 146+10 - 130+00	6 days	Wed 5/24/23	Wed 5/31/23	31	34
34			TNC WATERMAIN	4 days	Thu 6/1/23	Tue 6/6/23	33	35
35			TIE IN W/M @ BUGER	1 day	Wed 6/7/23	Wed 6/7/23	34	36SS
36			INSTALL SERVICES 23 EA.	7 days	Wed 6/7/23	Thu 6/15/23	35SS	38
37			**TRIPOLI ST.& TRIPOLI COURT**	**11 days**	**Fri 6/16/23**	**Fri 6/30/23**		
38			INSTALL W/M 171+50 - 164+25 TRIPOLI ST.	4 days	Fri 6/16/23	Wed 6/21/23	36	39
39			INSTALL W/M 174+75 - 173+ 00 TRIPOLI CT.	1 day	Thu 6/22/23	Thu 6/22/23	38	40,44
40			TNC WATERMAIN	4 days	Fri 6/23/23	Wed 6/28/23	39	41
41			TIE IN @ TUSCANY	1 day	Thu 6/29/23	Thu 6/29/23	40	42SS
42			INSTALL SERVICES 7EA.	2 days	Thu 6/29/23	**Fri 6/30/23**	41SS	
43			**CIMARRON DR.**	**13 days**	**Fri 6/23/23**	**Tue 7/11/23**		
44			INTALL W/M 151 +00 - 161+00	4 days	Fri 6/23/23	Wed 6/28/23	39	45,49
45			TNC W/M	4 days	Thu 6/29/23	Tue 7/4/23	44	46
46			TIE IN @ TUSCANY	1 day	Wed 7/5/23	Wed 7/5/23	45	47
47			INSTALL SERVICES 16 EA.	4 days	Thu 7/6/23	Tue 7/11/23	46	
48			**TANGLEWOOD DR**	**27 days**	**Thu 6/29/23**	**Fri 8/4/23**		
49			INSTALL W/M 66+50 - 41+50	11 days	Thu 6/29/23	Thu 7/13/23	44	50,54
50			TNC W/M	4 days	Fri 7/14/23	Wed 7/19/23	49	51
51			TIE IN W/M @ BURGER	1 day	Thu 7/20/23	Thu 7/20/23	50	52,65
52			INSTALL SERVICES 39 EA	11 days	Fri 7/21/23	Fri 8/4/23	51	58
53			**TRICKLEWOOD DR. & TRICKLEWOOD COURT**	**24 days**	**Fri 7/14/23**	**Wed 8/16/23**		
54			INSTALL WATER MAIN 104+50 - 87+00 TRICKLEWOOD DR.	6 days	Fri 7/14/23	Fri 7/21/23	49	55
55			INSTALL W/M 109+25 - 117+00 TRICKLEWOOD CT.	3 days	Mon 7/24/23	Wed 7/26/23	54	56,60
56			TNC W/M	4 days	Thu 7/27/23	Tue 8/1/23	55	57
57			TIE IN W/M @ TANGLWOOD DR	1 day	Wed 8/2/23	Wed 8/2/23	56	58
58			INSTALL SERVICES 30 EA.	8 days	Mon 8/7/23	Wed 8/16/23	57,52	
59			**BROOKHILLS COURT**	**9 days**	**Thu 7/27/23**	**Tue 8/8/23**		

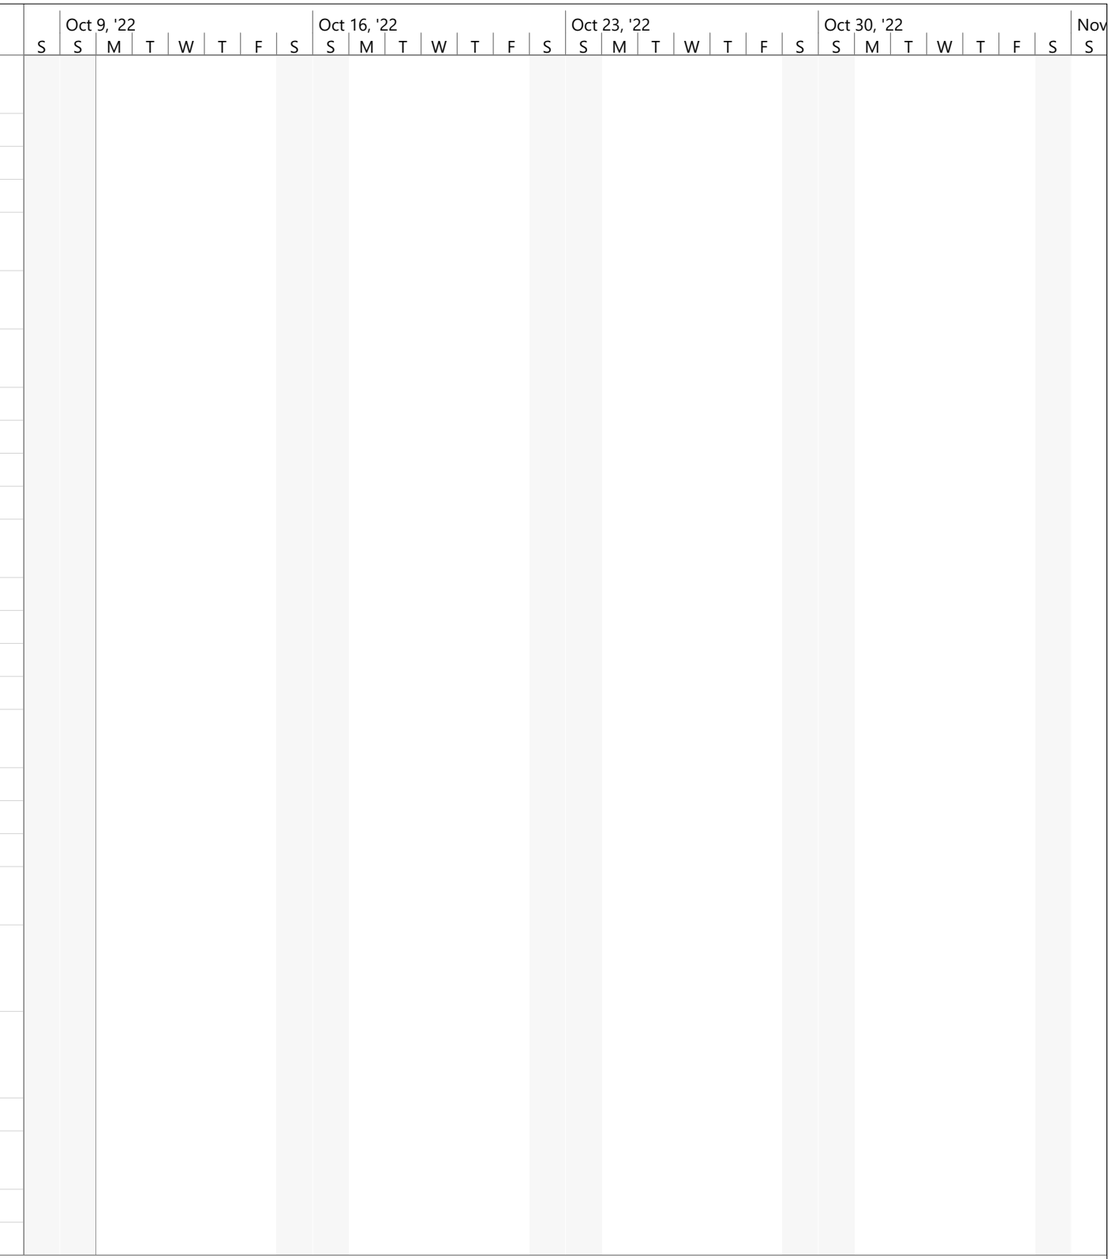

Project: Progress Schedule fall
Date: Tue 9/27/22

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors
60			INSTALL W/M 119+60 - 123+00	2 days	Thu 7/27/23	Fri 7/28/23	55	61
61			TNC W/M	4 days	Mon 7/31/23	Thu 8/3/23	60	62
62			TIE IN W/M @ TANGLEWOOD	1 day	Fri 8/4/23	Fri 8/4/23	61	63
63			INSTALL SERVICES 6 EA	2 days	Mon 8/7/23	Tue 8/8/23	62	
64			**ROAD WORK SECTION**	**51 days**	**Fri 7/21/23**	**Fri 9/29/23**		
65			GRADE FOR C/G	5 days	Fri 7/21/23	Thu 7/27/23	51	66
66			POUR C/G	5 days	Fri 7/28/23	Thu 8/3/23	65	67
67			GRADE ROAD CROSSINGS	4 days	Fri 8/4/23	Wed 8/9/23	66	68
68			GRADE BIT/CONCRTE DRIVES	15 days	Thu 8/10/23	Wed 8/30/23	67	69,70
69			PAVE BIT DRIVES	6 days	Thu 8/31/23	Thu 9/7/23	68	
70			POUR CONCRETE DRIVES	8 days	Thu 8/31/23	Mon 9/11/23	68	71SS+1 day
71			PLACE TOPSOIL	8 days	Fri 9/1/23	Tue 9/12/23	70SS+1 day	72
72			IRRIGATION REPAIRS	8 days	Wed 9/13/23	Fri 9/22/23	71	73
73			FINAL RESTORATION	5 days	Mon 9/25/23	Fri 9/29/23	72	

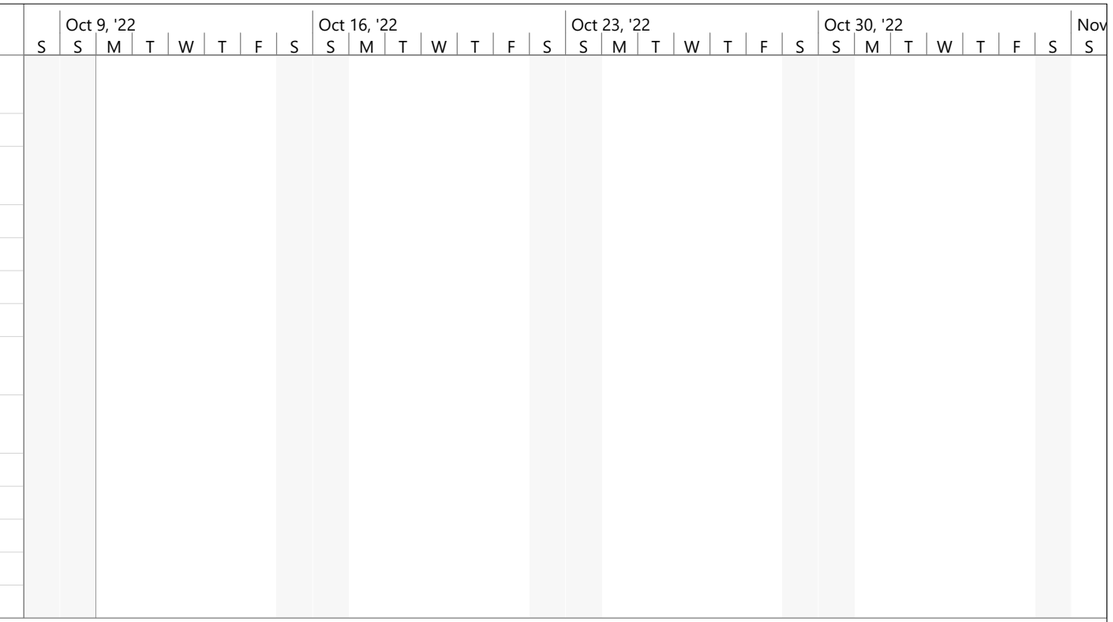

Project: Progress Schedule fall
Date: Tue 9/27/22

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
